1st & Final Bill

BR No. 461
26/15/16

M. A. R. 57 (Rule 116)

Measurement Book

No. B 489107

Serial No. Other roads, Mallasandra in ward No. 13, in Shettyhalli Sub Division

Name of Work construction of RCC drain near old Tunjappa Temple surrounding area & ..... From ..... To .....

Name of Contractor of nature of Agency ..... Technical Manager (Ward) KRIDL .....

Date of commencement of work .....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Job code:- 01347-000012				Est. cost:-50.00 lakhs		
	A.A.No:- AC/DZ/AS/30/2016-17. Dt. 30.08.2016.						
	T.S.No:- CE/DZ/TS/40/2016-17, dt 01.09.2016.						
	W.O.No:- BBMP/EE/DD/WO/65/2016-A. Dt. 02.09.2016.						
	Date of recording:- 19-9-16						
①	Earthwork excavation by manual means in ordinary soil involving an average horizontal throw upto 2m & an average lift upto 1.5m, excavated surface levelled & sides neatly dressed, the disposed earth to be levelled neatly after breaking of clods complete as per specifications as per Pre-measurement & recorded in this MB page No. 489172 vide item No ① -					453.24 Cum	

M. A. R. 57 (Rule 116)

Measurement Book

No. B 489108

Serial No. .....

Name of Work ..... From..... To.....

Name of Contractor of nature of Agency .....

Date of commencement of work .....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1.	2	3	4	5	6	7	8
	aggregate @ 0.69 cum and fine aggregates @ 0.460 cum with Super plasticisers @ 3 ltrs confirming to IS 9103-1999 reafirmed -2008, machine mixed, concrete laid in layers not exceeding 15 cms thick, vibrated for all works in foundation for footings, podastals, retaining walls, stair case, returnwalls, walls (any thickness) including attached plasters, columns, biers, abutments, pillars posts, struts, buttresses, string or lacing courses parapets, bed blocks, anchor blocks, plain window cills, fillets etc. including cost of all materials, labour, HOM of machinery, curing complete as per specifications. As per pre measurement Bk recorded in this MB page No. 489178 vide item NO (3). i.e. @ Rate of 6198.12/cum				245.96 cum = ₹ 15,24,503/-	15,24,490/-

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
				Sub total		= ₹45,35,128/-	
				KRIDL charges 8%		= ₹ 3,62,810/-	
				QC 1%		= ₹ 50,000/-	
					Total	= ₹ 49,47,938/-	
						4534808-	
						362784=	
						4897592=	

Certificate:

① The works done by contractor satisfactorily

② The contractor has removed all debris from work spot

③ There is no departmental issues.

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಶಿಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಎಸ್.ಎಂ. ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ...

AE
19-9-21

Serial No. .....
Name of Work .....
Name of Contractor
Date of commencem

Date	Full desc
1	

M. A. R. 57 (Rule 116)
Measurement Book

No. B 489112

Serial No. .....

Name of Work ..... From..... To.....

Name of Contractor of nature of Agency .....

Date of commencement of work .....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
		N					

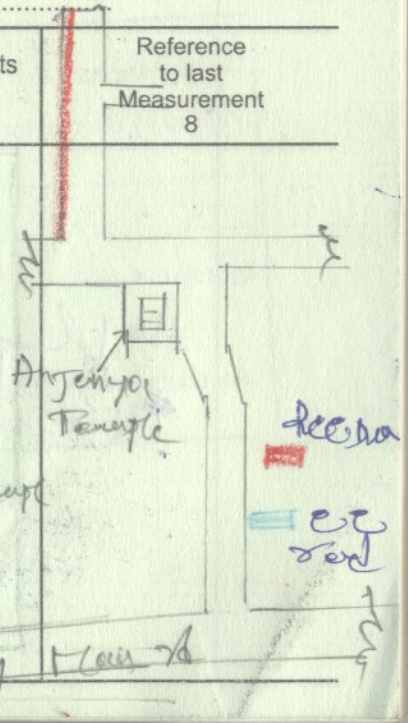

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Audited and admitted for Rs. 4897592= Passed by Cheque for Rs. 4256419= (.....) by adjustment Rs. 641173= Accounts Superintendent 14/11/16 Executive Engineer B.B.M.P. Hegganahalli Division						

Serial No. .....
Name of Work ....
Name of Contract
Date of commenc

Date	Full de
1	

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Audited and admitted for Rs. 4897592= Passed by Cheque for Rs. 4256419= (.....) by adjustment Rs. 641173= Accounts Superintendent 14/11/16 Executive Engineer B.B.M.P. Hegganahalli Division						

Serial No. .....
Name of Work ....
Name of Contract
Date of commenc

Date	Full de
1	
